



Capital Projects Report to the

Citizens' Oversight Committee



COVID-19 Response

- Mitigation Measures continue at active sites
- Impacts to project completion schedules due to supply chain interruptions for:
 - Greenhouse Replacement
 - VRC/SAC
- 2 days lost due to COVID-19 close-contact at New Instructional Building - Recovery schedule underway

Current IPP and FPP Status

Cypress	Fullerton	Anaheim
Fine Arts Building Renovation (FPP)	New Performing Arts Complex (FPP)	Upper Deck Parking Lot (IPP/FPP)
Career & Technical Education Complex (IPP)	STEM Vocational Center (IPP)	

Questions

Next: Cypress College

PROJECTS IN PLANNING, PROGRAMMING, DESIGN, AND CONSTRUCTION

り

- Campus Site Plans
- Project Status Reports

Aerial View - Cypress Campus



Phase

Initial Project Proposal (IPP)

Design

Construction

Close-Out

Cypress College

New SEM

- Building envelope completed with window & door installation done
- Interior casework installation at labs underway
- Classrooms nearing completion
- Landscaping around the building



Cypress College

VRC/SAC

- Substantial Completion
- Commissioning Completed
- Punch-List Being Addressed
- Furniture, fixtures and equipment installation completed
- Change Order #03 approved



Cypress College

Veterans' Memorial Bridge, Plaza, and Tribute Garden

• Punch-list items completed

Pond Refurbishment

- Pond equipment fully functional
- Punch-list items completed



Campus Projects' Safety Report

Information provided by Sundt Construction on February 10, 2021

Classification	Total Incidents	Incidents This Quarter	Sample
First Aid	15	0	11/5/20 - Scratch
Safety Stand Down	6	0	11/15/20 - Standing on mid rail of Scissor Lift
Near Miss	15	0	7/24/20 - Walking under a load
Equipment	5	0	10/29/20 - Line strike grounding SEM Building
Recordable	4	0	6/2/20 - Back Strain

Athletic Field Realignment -**Baseball Field Improvements**

- Substantial Completion achieved in early January 2021
- Punch-list items remaining
- Close-Out underway



Photograph taken February 3, 2021

Updates on campus projects - Cypress College

Fine Arts Building Renovation

- Programming and Preliminary Plans Completed
- Preliminary Plans Submitted to State in January 2021 and approved in late February 2021
- Working Drawings in progress



Updates on campus projects - Cypress College

Central Plant Enhancements

Project in close-out phase.

Security Cameras

- Guidepost Solutions completed work on the assessment of the campus security system and development of campus wide security system standards
- Campus establishing scopes of work for upcoming projects

Questions

Next: Fullerton College

Aerial View - Fullerton Campus



Phase Initial Project Proposal (IPP) Planning / Design Bidding Construction Close-Out

Fullerton College

New Instructional Building

- Exterior framing nearing completion
- Window and door installation underway
- Interior drywall and painting
- Roof clay tile installation in progress



Fullerton College

Central Plant Replacement and Expansion

- Building exterior completed
- Piping and connection of chillers and cooling towers
- Energization in upcoming month



Campus Projects' Safety Report

Information provided by BN Builders on February 10, 2021

Classification	Total Incidents	Incidents This Quarter	Sample
First Aid	0	0	N/A
Safety Stand Down	0	0	N/A
Near Miss	1	0	5/15/20 - Utility strike on underground (no injuries)
Equipment	1	0	4/21/20 - Excavation wall blowout (no injuries)
Recordable	2	1	12/17/2020 – Lower Back Sprain (no lost time)

Greenhouse Replacement & Bathroom Remodel

- ADA-compliant remodel to bathrooms complete
- New greenhouse installation nearing completion
- Sitework in progress



Photograph taken February 3, 2021

Renovate Buildings 300 & 500

- Bidding completed on February 16th, 2021 firms submitted bids for consideration
- Bids will be rejected at the March 9th Board meeting
- Evaluation Process Underway
- Construction Anticipated to Start in January 2022



Chapman / Newell Instructional Building and New M&O Building


- Board of Trustees Approved use of Design-Build for the project
- Project Planning Completed
- RFP/Q for Design-Builders in Q2-2021
- Target Construction Start Spring of 2023



Performing Arts Complex & Demolition Buildings 1100 and 1300

- Pfeiffer Partners Architects Selected as Architect of Record.
- Preliminary Plans to started on February 5th, 2021
- Anticipated completion of Preliminary Plans by end of April 2021






Redesigned Campus Project Webpage

https://vpas.fullcoll.edu/home/campus-projects-home/

Questions

Next: Anaheim - NOCE Campus

Aerial View - Anaheim Campus

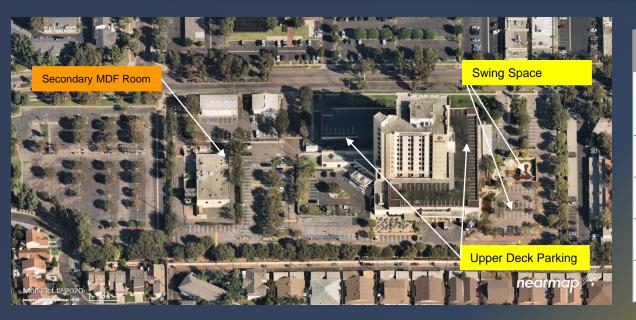

Phase

Combined Initial & Final Project Proposal (IPP/FPP)

Planning / Design

Bidding

Construction

Close-Out

Updates on campus projects - Anaheim Campus

Swing Space / Interim Housing

 Planning for temporary relocation of NOCE classrooms & Culinary Arts

Upper Deck Parking Lot Refurbishment

 IPP/FPP under review at the State Chancellor's Office for funding

Secondary MDF Room

Construction completed. Additional IT equipment installation underway



Questions

Next: District-Wide IT Network Refresh

Updates on campus projects - IT Network Refresh

IT Network Refresh at Cypress, Fullerton, and Anaheim Campuses

- Change Order 02 for upcoming Phase II of Project: Installation of additional switches, cabling, outdoor wireless, UPS's and PDU's
- Installation of telecommunication conduits and cabling for the New Instructional Building and Central Plant at Fullerton College
- Project not part of OCIP Safety up to vendor (VectorUSA)

Questions

Financial Review

Financial Review

30

- Capital Projects Update
- Estimated Project Budgets
- 90-Day Look Ahead Schedule

North Orange County Community College District Measure J Capital Projects Update As of January 31, 2021

Bond Authorization:

Bond Funding Sources (Budget):

Bond Authorization	574,000,000	100.00%
Bonds Sold - Series A + B	250,000,000	43.55%
Available Principal Amount of Bonds	324,000,000	56.45%

		Actual Received	Remaining Balance
Bond Authorization	574,000,000	250,000,000	324,000,000
Estimated Net Interest Earnings	11,000,000	8,888,259	2,111,741
Totals	585,000,000	258,888,259	326,111,741

Cost Status:

Campus	Total Budget	%	Actual Expenses to Date	Remaining Balance
Anaheim Campus	23,607,800	4.04%	2,320,111	21,287,689
Cypress Campus	225,921,200	38.62%	93,857,770	132,063,430
Fullerton Campus	311,126,400	53.18%	33,101,307	278,025,093
District Expenses				
Program Management	20,000,000	3.42%	4,935,394	15,064,606
Bond Issuance Cost	3,544,600	0.60%	1,301,760	2,242,840
Other Bond Expense	800,000	0.14%	338,343	461,657
Totals	585,000,000	100.00%	135,854,685	449,145,315

PROJECT BUDGET/VARIANCE REPORT—CYPRESS

	Т	Measure			Measure J						
	1	Budget			Budget				Measure J		
CURRENT PROJECTS	┸	NOV FY 202			N FY 2020-21		Variance		Expenses		Balance
New Science, Engineering, and Mathematics Building	\$			\$	94,322,272		121	\$	73,712,026		20,610,246
New Veterans' Resource Center & Student Activities Center Expansion	\$	13,500,000		\$	13,500,000	\$.53	\$	10,747,785		2,752,215
Veterans' Memorial Bridge and Tribute Garden	\$	100,800		\$		\$	100	\$		\$	100,800
Fine Arts Building Renovation *	\$	16,764,338		\$		\$	HC.	\$	-	\$	16,764,338
Update/Improve Infrastructure	\$	14,418,406	1 & 6	\$	14,418,406		100	\$	-	\$	14,418,406
Update/Improve Infrastructure (New SEM)	\$	2,801,641		\$		\$	2	\$	2,573,569		228,072
Update/Improve Infrastructure (IT)	\$	6,000,000		\$	5,101,587	\$	(898,413)	\$	1,520,769		3,580,818
Update/Improve Infrastructure (VRC/SAC)	\$	1,055,923	1 & 6	\$	1,055,923	\$		\$	1,206,906		(150,983)
Update/Improve Infrastructure (IT - VRC/SAC)	\$		2,5 & 7	\$	252,530	\$	252,530	\$	10,000	\$	242,530
Update/Improve Infrastructure (IT - New SEM)	\$	(*)	5	\$	645,883	\$	645,883	\$		\$	645,883
Planning (Non Project Specific)	\$	520,000		\$		\$	121	\$	150,807		369,193
Library-Learning Resource Center Expansion	\$	15,000,000		\$	15,000,000	\$	-	\$	38,665	\$	14,961,335
Swing Space Projects	\$	3,236,521		\$	3,236,521	\$.52	\$	2,202,518	\$	1,034,003
Mass Communications & Security Systems Upgrade	\$	4,026,889	-4	\$	3,942,855	\$	(84,034)	\$		\$	3,942,855
Mass Communications & Security Systems Upgrade (New SEM)	\$	305,333	4	\$	389,367	\$	84,034	\$	245,869	\$	143,498
Mass Communications & Security Systems Upgrade (VRC/SAC)	\$	60,938		\$	60,938	\$	W.	\$	54,671	\$	6,267
Campus-Wide Security Systems Upgrade	\$	58,670		\$	58,670	\$	126	\$	2	\$	58,670
Pool Restoration and Upgrade	\$	4,876,000		\$	4,876,000	\$		\$		\$	4,876,000
Gym I/Gym II Restoration and Restrooms	\$	4,837,500		\$	4,837,500	\$	100	\$	-	\$	4,837,500
Gateway Phase 1	\$	5,810,000		\$	5,810,000	\$	H.	\$	-	\$	5,810,000
Under Piazza & Stairwell Restoration	\$	1,963,800		\$	1,963,800	\$		\$		\$	1,963,800
Tech I/Tech III Capital Improvements★	\$	27,645,342		\$	27,645,342	\$	120	\$	2	\$	27,645,342
Athletic Field Realignment/Entry Revisions/Parking Lot Improvements	\$	6,435,394	3	\$	6,425,314	\$	(10,080)	\$		\$	6,425,314
Baseball Field Improvements	\$	1,922,901	3	\$	1,932,981	\$	10,080	\$	1,139,002	\$	793,979
	C	OMPLETED P	ROJEC	TS							
Update/Improve Infrastructure (Central Plant Enhancements)	Ts	61,862		\$	61,862	\$		\$	58,513	\$	3,349
Mass Communications & Security Systems Upgrade (Safety Film)	\$	145,772		\$	145,772			\$	145,772		-
Mass Communications & Security Systems Upgrade (Door Replacement		50,898		\$		\$	-	\$	50,898		(*)
	Τ										
SUB TOTAL	9	225,921,200		s	225,921,200	s	-	s	93,857,770	9	132.063.430

NOTES:

- 1. Project Encumbrance Transfer Request 2021-022 CC -Required to allocate funds attributed to the Update/Improve Infrastructure VRC-SAC project budget per approved Sundt Construction P0131052 CO#2 BOT approved 07/28/20 PCO-V0250 \$21,989
- 2. Project Encumbrance Transfer Request 2021-023 CC Required to create and realign the Update/Improve Infrastructure (IT -VRC-SAC) project budget for clairty & tracking
- 3. Project Encumbrance Transfer Request 2021-025 CC Required to allocate funds to the Baseball Field Improvements project. Amend #1 was issued to Vital Inspection, Inc. P0139938 \$10,080 provide additional Inspector of Record (IOR) Services.
- 4. Project Encumbrance Transfer Request 2021-026 CC Required to allocate funds attributed to the approval of Sundt Construction Co., CO#3 P0131052 Board Approved 11/10/20 SEM Security Camera's, cable, and hardware.
- 5. Project Encumbrance Transfer Request 2021-027- CC Required to allocate funds attributed to the approval of Sundt Construction Co., CO#3 P0131052 Board Approved 11/10/20 IT Upgrades to match Districtwide Infrastructure projects and new District Standards.
- 6. Project Encumbrance Transfer Request 2021-030- CC Required to Reverse Project Encumbrance Transfer Request 2021-022 CC
- 7. Project Encumbrance Transfer Request 2021-031- CC Required to allocate funds attributed to the approval of Sundt Construction Co., CO#2 P0131052 Board Approved 07/28/20 PCO-V0250 \$21,989 IT Network Refresh

* Denotes projects with additional State funds in budget- Refer to project page on COC Report for additional details

PROJECT BUDGET/VARIANCE REPORT—FULLERTON

CURRENT PROJECTS		leasure J Bu NOV FY 2020			Measure J Budget N FY 2020-21	Variance	Measure J Expenses	Balance
Greenhouse Replacement	\$	834,381		\$	834,381	\$ -	\$ 342,913	\$ 491,468
New Instructional Building	\$	53,588,031		\$	53,588,031	\$ § 1	\$ 23,595,962	\$ 29,992,069
Central Plant Replacement & Expansion	\$	10,600,000		\$	10,600,000	\$ -	\$ 5,521,415	\$ 5,078,585
Renovate Buildings 300 & 500 *	\$	20,482,000		\$	20,482,000	\$ -	\$ 944,391	\$ 19,537,609
New M & O Building	\$	6,758,944		\$	6,758,944	\$ 	\$ 6,625	\$ 6,752,319
Chapman / Newell Instructional Building	\$	21,985,777		\$	21,985,777	\$ -	\$ 6,625	\$ 21,979,152
New Performing Arts Complex—Demolish Buildings 1100 and 1300	\$	30,724,153		\$	30,724,153	\$ -	\$ 0=0	\$ 30,724,153
New Welcome Center & Lot C West	\$	37,353,872		\$	37,353,872	\$ -	\$ 12	\$ 37,353,872
New Horticulture/Lab School/STEM Lab	\$	33,813,764		\$	33,813,764	\$ 8	\$ -	\$ 33,813,764
Renovate Building 840 Campus Services	\$	7,878,400		\$	7,878,400	\$ -	\$ 100	\$ 7,878,400
Demolish Building 2000	\$	1,108,000		\$	1,108,000	\$ 	\$ 196	\$ 1,108,000
New Parking Structure	\$	11,219,260		\$	11,219,260	\$ u	\$ 020	\$ 11,219,260
Update/Improve Infrastructure	\$	23,110,416		\$	23,110,416	\$ -	\$ 0.70	\$ 23,110,416
Update/Improve Infrastructure (IT)	\$	8,000,000	1	\$	7,721,018	\$ (278,982)	\$ 1,964,873	\$ 5,756,145
Update/Improve Infrastructure (IT - New Instructional Bldg.)	\$	121	1	\$	278,982	\$ 278,982	\$ 	\$ 278,982
New Thermal Energy Storage (TES)	\$	10,139,524		\$	10,139,524	\$ 8	\$ 18	\$ 10,139,524
Renovate Building 600	\$	3,117,641		\$	3,117,641	\$ -	\$ 1.00	\$ 3,117,641
Renovate Health Center	\$	1,328,800		\$	1,328,800	\$ -	\$ 19	\$ 1,328,800
Renovate Faculty Lounge & Offices	\$	6,212,250		\$	6,212,250	\$ =	\$ 020	\$ 6,212,250
Renovate Wellness Center	\$	2,534,400		\$	2,534,400	\$ -	\$ 0572	\$ 2,534,400
Landscape & Hardscape Improvements	\$	3,840,000		\$	3,840,000	\$ -	\$ 0=0	\$ 3,840,000
Renovate Building 3100	\$	2,402,940		\$	2,402,940	\$ -	\$ 72	\$ 2,402,940
Demolish Building 1901-04, 1956-60, 3000	\$	1,333,000		\$	1,333,000	\$ E 1	\$ 18	\$ 1,333,000
Parking Lot Improvements at Building 3000	\$	1,999,500		\$	1,999,500	\$ -	\$ 180	\$ 1,999,500
Renovate Building 2100	\$	8,277,500		\$	8,277,500	\$ -	\$ 196	\$ 8,277,500
Demolish Buildings 2200 & 3104	\$	1,392,209		\$	1,392,209	\$ =	\$ 020	\$ 1,392,209
Planning (Non Project Specific)	\$	595,000		\$	595,000	\$	\$ 231,347	\$ 363,653
	С	OMPLETED I	PROJE	CT	S			
Update/Improve Infrastructure (Bldg 300-500 Sewer Line)	\$	496,638		\$	496,638	\$ -	\$ 487,156	\$ 9,482
SUB TOTAL	\$	311,126,400		\$	311,126,400	\$	\$ 33,101,307	\$ 278,025,093

NOTES:

33

^{1.} Project Encumbrance Transfer Request 2021-028-FC- Required to allocate funds attributed to the approval of BN Builders, Inc. - P0138124 - CO#1 - Board Approved 01/26/21 - Added services for the design of the Wireless Access Points (WAP's) in the Instructional Building.

^{*} Denotes projects with additional State funds in budget- Refer to project page on COC Report for additional details

CURRENT PROJECTS

PROJECT BUDGET/VARIANCE REPORT—ANAHEIM

CURRENT PROJECTS	ı	Measure J Bu NOV FY 2020		J	Measure J Budget AN FY 2020-21	Variance	Measure J Expenses	Balance
Update/Improve Infrastructure	\$	668,933	4	\$	661,133	\$ (7,800)	\$ -	\$ 661,133
Update/Improve Infrastructure (IT)	\$	1,000,000		\$	1,000,000	\$ -	\$ 650,593	\$ 349,407
Update/Improve Infrastructure (Secondary MDF)	\$	97,607	4	\$	105,407	\$ 7,800	\$ 60,832	\$ 44,575
Develop Interior and Exterior Signage	\$	313,800		\$	313,800	\$	\$	\$ 313,800
Second Floor Tenant Improvements	\$	813,000		\$	813,000	\$ -	\$ -	\$ 813,000
Swing Space Projects/ Interim Housing	\$	358,887	1,2&3	\$	2,000,000	\$ 1,641,113	\$ -	\$ 2,000,000
Upper Parking Lot Remodel *	\$	2,183,000		\$	2,183,000	\$ <u> </u>	\$ 42,503	\$ 2,140,497
Upper Deck Enhancements	\$	309,901		\$	309,901	\$ =	\$ 	\$ 309,901
1st. Floor Remodel Student Center and Classrooms	\$	2,352,720		\$	2,352,720	\$ -	\$ -	\$ 2,352,720
Pedestrian and Vehicular Traffic Flow	\$	3,329,000	- 1	\$	2,329,000	\$ (1,000,000)	\$ -	\$ 2,329,000
4th Floor Improvements	\$	218,000		\$	218,000	\$ =	\$ =	\$ 218,000
Outdoor Patio Remodel	\$	1,382,500		\$	1,382,500	\$ -	\$ = 1	\$ 1,382,500
Develop Drop-Off Plaza at Romneya Drive	\$	1,069,000	2	\$	569,000	\$ (500,000)	\$ -	\$ 569,000
Develop Intersection at Romneya & Coronet	\$	914,744	3	\$	773,631	\$ (141,113)	\$ <u> </u>	\$ 773,631
Holding Account	\$	6,600,000		\$	6,600,000	\$ 8	\$ ĕ	\$ 6,600,000
Planning (Non Project Specific)	\$	440,000		\$	440,000	\$ -	\$ 9,475	\$ 430,525
	1775.1	COMPLETE	D PRO	IEC.	TS			
7th and 10th Floors Buildout	\$	915,972		\$	915,972	\$ 	\$ 915,972	\$
5th Floor CTE & 2nd Floor Room 215	\$	640,736		\$	640,736	\$ Ē	\$ 640,736	\$
SUB TOTAL	\$	23,607,800		\$	23,607,800	\$ -	\$ 2,320,111	\$ 21,287,689

NOTES:

- 1. Project Encumbrance Transfer Request 2021-018-AC- Required to realign the Swing Space Project/ Interim Housing project budget as a result of cost evaluations in relation to Design, construction, rental, and dismantling of modular buildings for the relocation of classrooms and facilities on the first floor of the Anaheim- NOCE campus.
- 2. Project Encumbrance Transfer Request 2021-019-AC- Required to realign the Swing Space Project/ Interim Housing project budget as a result of cost evaluations in relation to Design, construction, rental, and dismantling of modular buildings for the relocation of classrooms and facilities on the first floor of the Anaheim- NOCE campus.
- 3. Project Encumbrance Transfer Request 2021-020- Required to realign the Swing Space Project/ Interim Housing project budget as a result of cost evaluations in relation to Design, construction, rental, and dismantling of modular buildings for the relocation of classrooms and facilities on the first floor of the Anaheim NOCE campus.
- 4. Project Encumbrance Transfer Request 2021-029-AC- Required to allocate funds to the Secondary MDF project. CO#1 was issued to Rodriguez Engineering P0139176 in the amount of \$7,800.

* Denotes projects with additional State funds in budget- Refer to project page on COC Report for additional details

PROJECT BUDGET/VARIANCE REPORT—DISTRICT

DISRICT WIDE EXPENSE	N	Measure J Budget DV FY 2020-20	21	1800	Measure J Budget N FY 2020-21	Variance	Measure J Expenses	Balance
Program Management Fees	\$	20,000,000		\$	20,000,000	\$ 20	\$ 4,935,394	\$ 15,064,606
Bond Issuance Cost	\$	3,544,600		\$	3,544,600	\$ -	\$ 1,301,760	\$ 2,242,840
Other	\$	800,000		\$	800,000	\$ -	\$ 338,343	\$ 461,657
SUB TOTAL	\$	24,344,600		\$	24,344,600	\$	\$ 6,575,497	\$ 17,769,103





CYPRESS - FULLERTON - ANAHEIM (NOCE)

90-DAY LOOK AHEAD SCHEDULE (02-01-21 TO 04-30-21)

	L	Febr	uary	1		Ma	rch		30	Apr	lin		Comments
	2	91	6 2	3	21	9 1	6 23	30	6	13 20	27	7	
SENERAL			-					,		- , -	,		
NOCCCD Board Meetings	П	T	П	П	П			П		Ш	П	П	
COC Meetings	Ш	П	П	П			П	П	П	Ш	П	Ш	March 3rd, 2021 (Meetings held via Zoom)
Bond Program Management Team Mtgs.	Ш			П			П	П	П	Ш	П	П	February 16th and March 16th (Meetings held via Zoom)
PLANNING			0.00	-							and a	-	A TOPPONE WE UNDERSONDER TO THE WHOLE SEATON
AN AHEIM (NOCE)	-	_				_	-			_	-	_	
Upper Deck Parking Lot Refurbishment DESIGN PHASE			-	- 0	- 4				8 8	-	_		Final Project Proposal (FPP) Under Review at CCCCO
CYPRESS				_									
Fine Arts Building Renovation				100			100	9	ÿ			111	
Preliminary Plans	П	Т	Т	Т	П	Т	Т	П	П	Т	Т	П	Complete
CCCO Review of Preliminary Plans							Т			\neg	т	П	In Progress
Working Drawings	П												Upcoming - Start upon Approval from CCCCO
FULLERTON				_					1/-		_		
New Performing Arts Complex													
RFP far Architect of Record		3 3							1				Complete
Preliminary Plans			4										In Pragress - Design Kick-off Meeting on 2/5/2021
CCCO Review of Preliminary Plans						T				T			Upcoming
DSA PHASE & AGENCY REVIEW													militario de la companya della companya della companya de la companya de la companya della compa
CYPRESS	Т												
New SEM - Deferred Approvals	1									Т	Т	П	Submittals forthcoming for DSA review and Approval
BIDDING		_	_	-		_	_				200	- 20	
FULLERTON					г								
Renovate 300-500 Buildings	+	_			-							$\overline{}$	
Bidding for Gen. Contractor		_	Ť	T		Ť	т		Т	Ť	Т	Ť	Complete
Bids Due & Evaluation Process		-	+	+		+	+	Н		+	+	Н	Bids Due on February 16th, 2021
Gen. Contractor Contract Award & NTP				-				Н	+	+	+	+	In Progress - Target Date to Award Contract is March, 24, 2021
PRE-CONSTRUCTION PHASE	-	_	_	-		_	_	_	_	_	_	_	III Flagress - ranget bate to Award contract is march, 24, 2021
	-			_				_					
CYPRESS					-	_	_	-		_	_	$\overline{}$	
Mass Communications - Security Cameras			10		- 31	_	\perp	ч		_	_	щ	Development of Scopes of Work
CONSTRUCTION PHASE	_												
CYPRESS	_				_			_				_	
Network Refresh	₽.	_		_	<u> </u>	_	_	-	_	_	_	_	
Phase I Design Implementation	\square	-	+	4		_	_	\vdash		_	\perp	\mathbf{H}	Complete
Phase II Design Implementation	\sqcup			┸									Planning In Progress
New SEM & Assoc. Mass Comm and Infra . Construction		_	_				_		1		_	_	
IDC Interior Framing and Finishes			8						8				In Progress
Building Envelope - Sheathing and Glass Installation			10			- 5					Г		Complete
Bathroom component installation											I	П	In Progress
Elevator mechanical room framing and rail component installation										\perp			In Progress
Electrical room wiring and transformer installation													In Progress
Voice, data, and fire alarm cabling													In Progress
Hardscaping around building site						1			2				In Progress
New VRC/SAC									8		_		
VRC Sundt Punch Walk and Final Finishes Repairs						Т				Т	Т	П	In Progress
SAC Sundt Punch Walk and Final Finishes Repairs						\perp	\top	П	\neg	\top	+	т	In Progress
Veterans' Memorial Bridge and Tribute Garden and Pond Refurb.						+	+	Н	\rightarrow	+	+	Н	Sundt Punch Walk and Final Finishes Regains Underway
Pand Refurbishment Punch List			10			+	+	Н	\rightarrow	+	+	+	Sundt Punch Walk and Final Finishes Repairs Underway
			_	-		_	-	-	\rightarrow	-	-	-	JRH and Westberg + White Punch Walk and Final Finishes Repairs

MAAS



NORTH ORANGE COUNTY COMMUNITY COLLEGE DISTRICT

CYPRESS - FULLERTON - ANAHEIM (NOCE)

90-DAY LOOK AHEAD SCHEDULE

(02-01-21 TO 04-30-21)

		Fel	orua	гу	L	N	larch	E.		A	pril		Comments
	2	9	16	23	2	9	16 2	23 30	6	13	20 :	27	1
ULLERTON					T								
laticulture Lab - Greenhouse Replacement	3 (4			100			- 0			0 10	_		
Installation of Greenhouse											_		Complete
Punch Walk and Final Repairs													RT Contractor and Westberg + White - In Progress
New Instructional Building	68	00 00								4,438	76.0	770	
Scaffolding and Exterior Wall Framing				- 1			1	7			ř.		Complete
Exterior Wall Sheathing, Waterproofing and Window Installation													In Progress
Mechanical, Electrical, and Plumbing Rough-In													In Progress
Interior Framing													In Progress
Building Roofing													In Progress
Interior Drywa II											- 19		In Progress
entra I Plant Expansion	88							100	8		-	525	
Installation of Underground Utilities		Ī							П				In Progress
Connection to Existing Utilities							8	1			Ų.		In Progress
Mechanical, Electrical, and Plumbing Rough-In													In Progress
Exterior Wall Sheathing, Waterproofing and Moulding					Т				П				Complete
Network Refresh		511	172		Т			700		-	- 1/2	- 37	
Phase I Design Implementation	8	7							П	2 4	Т	- 8	Complete
Phase II Design Implementation	88		- 8	- 6			3				8		Planning In Progress
Coordination for Greenhouse Components				3									In Progress
ANAHEIM (NOCE)	1											-	
and Main Distribution Frame (MDF) Room - Equipment													Nearing Completion
LOSE-OUT PHASE					Т		-						A STATE OF THE STA
NAHEIM (NOCE)					Т								
and Main Distribution Frame (MDF) Room for Campus	7			1	1						П		Upcoming
YPRESS	5/8	10.0		92	т								
Jpdate Infrastruture - Centra i Plant Enhancements				- 6				3		3	0	- 6	In Progress
Athletic Field Realignment - Baseball Clubhouse					Т								Upcoming upon completion of work
/RC/SAC			\neg	\neg									Upcoming
/eterans' Memorial Bridge and Tribute Garden and Pond Refurb.				\neg	Т				П				Upcoming
and Refurbishment				\neg									Upcoming
ULLERTON		61 6	100	62	т	10			Т				N A
Horticulture Lab - Greenhouse Replacement											TA2 II	- 0	Upcoming upon completion of work

Thank you!

Next Meeting: June 2nd, 2021
